



**AQUIND Limited**

---

## **AQUIND INTERCONNECTOR**

Compulsory Aquisition Hearing 1 – Appendix 1  
- Exhibit 21 Drawings showing the key stages of  
construction at Fort Cumberland Road Car Park

The Planning Act 2008

Infrastructure Planning (Examination Procedure) Rules 2010, Rule 8(c)

Document Ref: 7.9.18.21

PINS Ref.: EN020022

**Fort Cumberland Road Car Park**

66 weeks – Not continuous, and dependant on weather conditions

**Phase 1:** HDD Assumed all for ducts – 44 weeks, Q3 2021 to Q2 2022

75% of Car Park occupied




- - - - Order Limits  
  Indicative HVDC Cable Corridor  
  Indicative HVDC Cable route  
  HDD route


**PHASE 1**

**Phase 2:** Construct TJB for 1st circuit, pull onshore cables and offshore cables, joint and permanently reinstate – 5 weeks Q2 2022

50% of Car Park occupied

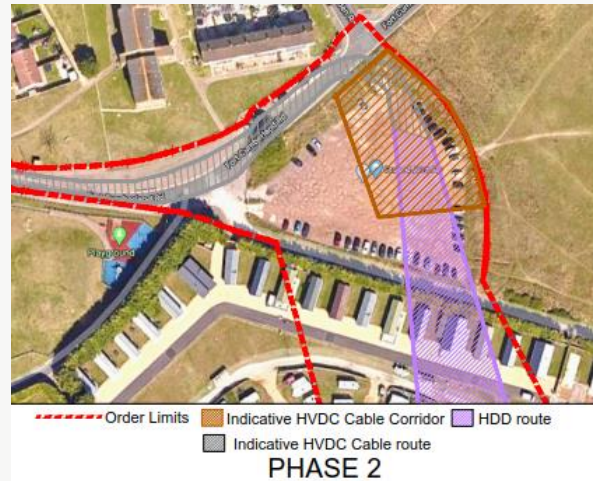


**Phase 3:** Car Park all clear

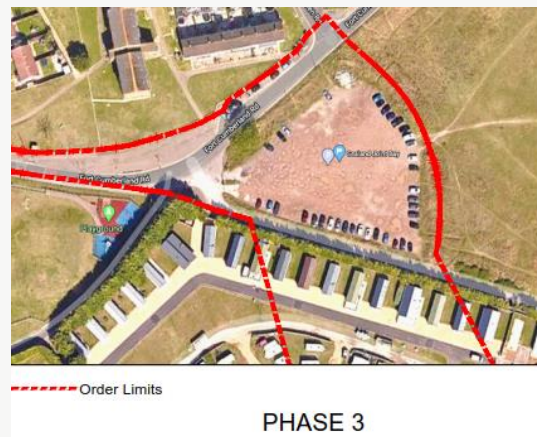

**Phase 4:** Construct TJB for 2<sup>nd</sup> circuit, pull onshore cables and offshore cables, joint and permanently reinstate


– 5 weeks Q3 2022

50% of Car Park occupied

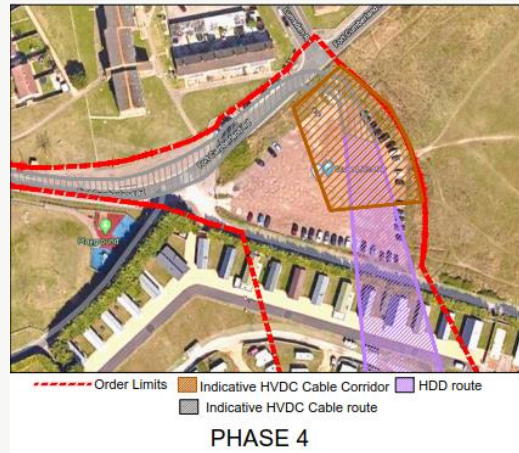

**Phase 5:** Construct ORS: - 12 weeks Winter 22/23

50% of Car Park occupied

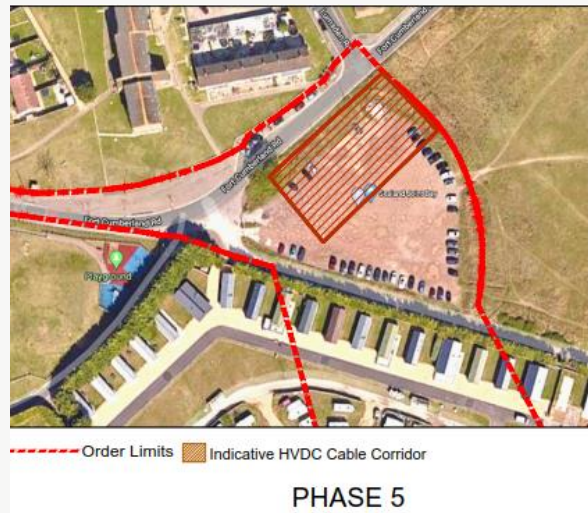

**Phase 6: Carpark all clear Q2 2023**



PHASE 6

\*Duration not consecutive

