

Thames Tideway Tunnel
Thames Water Utilities Limited



Application for Development Consent

Application Reference Number: WWO10001

Code of Construction Practice Part B

Doc Ref: **7.19.2**

Carnwath Road Riverside

APFP Regulations 2009: Regulation **5(2)(q)**

Hard copy available in

Box **56** Folder **B**
January 2013

**Thames
Tideway Tunnel**



Creating a cleaner, healthier River Thames

This page is intentionally blank

Thames Tideway Tunnel

Code of Construction Practice Part B

Carnwath Road Riverside

List of contents

	Page number
1 Carnwath Road Riverside.....	1
1.1 General.....	1
2 General Requirements.....	2
3 Communications and community/stakeholder liaison	2
4 Site operation	2
5 Public access, highway and river transport	3
6 Noise and vibration.....	4
7 Air quality	5
8 Water resources	5
9 Land quality	5
10 Waste management and resource use.....	6
11 Ecology (aquatic and terrestrial)	6
12 Historic environment	6
13 Other	6

List of figures

	Page number
Figure 1.1 Carnwath Road Riverside: Site context and location plan	2


This page left intentionally blank

1 Carnwath Road Riverside

1.1 General

- 1.1.1 All works covered within this document are to be managed and performed to the culture within the Thames Tideway Tunnel vision of 'Zero Accidents, Zero Harm, Zero Compromise'.
- 1.1.2 The *Code of Construction Practice (CoCP)* comprises two parts:
- a. Part A: General requirements. These measures are applicable project-wide.
 - b. Part B: Site-specific requirements. These are site-specific measures, where there are deviations from the general requirements indicated in Part A.
- 1.1.3 This document comprises the *CoCP* Part B for the Thames Tideway Tunnel Project works at Carnwath Road Riverside site and identifies the detailed site-specific measures including working hours, site set up and servicing arrangements, taking into account the environmental issues and consultations with the London Borough of Hammersmith and Fulham and other stakeholders.
- 1.1.4 For ease of reference the *CoCP* Part B mirrors the headings in Part A. The *CoCP* Part B sets out site-specific issues and deviations from Part A so where there are no site-specific measures reference should be made to the measures set out in Part A.
- 1.1.5 A plan showing the location of the site is shown in Figure 1.1 below.

Figure 1.1 Carnwath Road Riverside: Site context and location plan

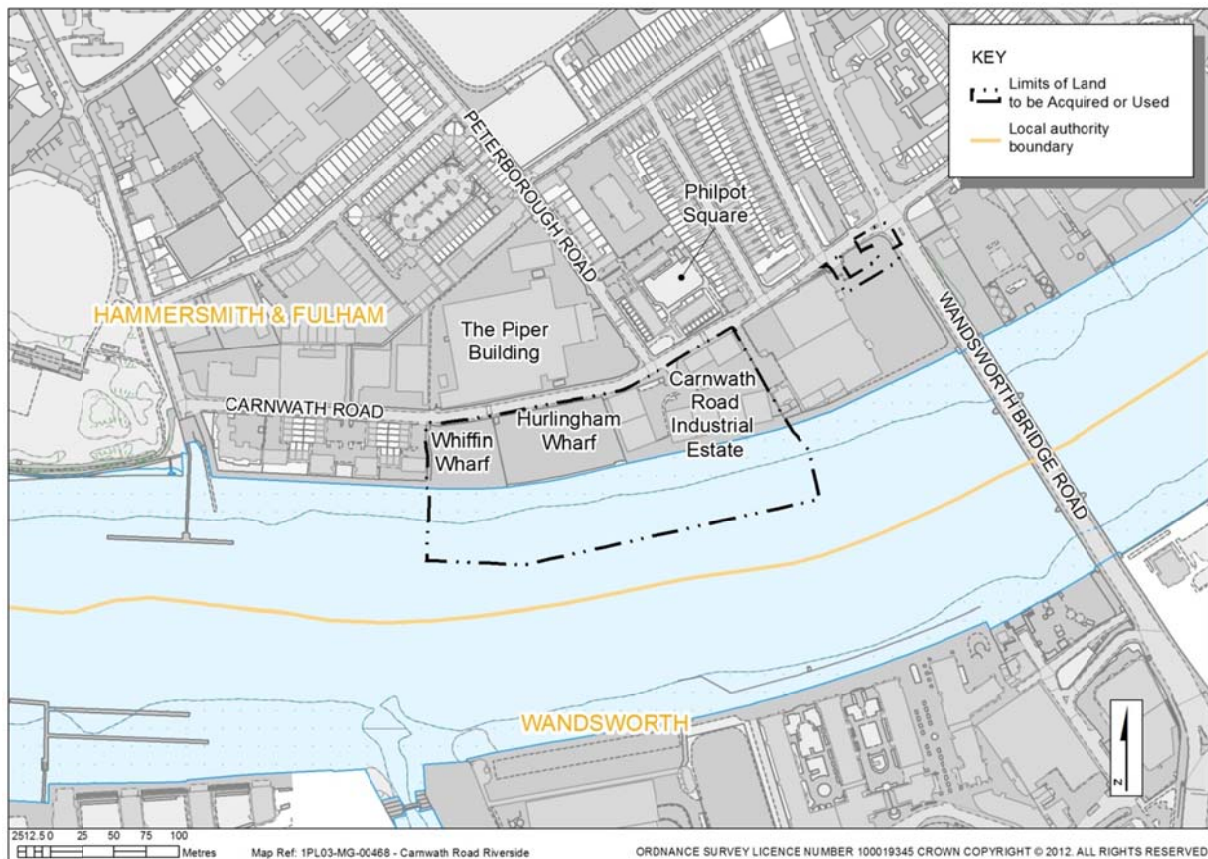

Note: For detailed Limits of Land to be Acquired or Used, refer to drawings in the Book of Plans.

2 General Requirements

2.1.1 As per text in CoCP Part A.

3 Communications and community/stakeholder liaison

3.1.1 As per text in CoCP Part A.

4 Site operation

Topic	Site-specific requirement
Working hours	<p>This site will adhere to the following working hours:</p> <ul style="list-style-type: none"> a. standard b. extended standard c. continuous for main tunnel construction works. <p>Other working hours are subject to agreement with the local authority.</p>

Topic	Site-specific requirement
Site layout	<p>The site layout will consider the use of required offices and storage containers as noise barriers.</p> <p>The layout of noise barriers and structures will also consider potential impacts</p>
Site security / hoarding requirements	<p>The hoarding is to be as defined in <i>CoCP</i> Part A para 4.3.4a incorporating suitable art work on public facing sections.</p> <p>5m high hoarding/noise barrier on western end of site and 7.5m on eastern end of site, 3.6m on the northern edge, and 2.4m on the southern edge (on the river side). Barriers on east/west end can be office /welfare facilities.</p>
Other items	<p>A site-specific lighting plan is required. The lighting will address the impact on terrestrial and aquatic ecology and include the use of low level directional lighting where possible whilst meeting safe work requirements.</p> <p>Works to reduce the foreshore level, build campsheds, and/or jetties, and strengthen existing river wall required at the start of the construction period to enable the use of river transport.</p>

5 Public access, highway and river transport

Topic	Site-specific requirement
Site access and gates	<p>The security barrier will be positioned to allow a standard rigid tipper vehicle to be wholly off the road whilst awaiting barrier operation.</p> <p>The western access will be only used for emergency access or specific deliveries and not routinely used due to proximity of adjacent properties.</p>
Traffic management	<p>All vehicles will access/egress the site from the Wandsworth Bridge Road (A217) and Carnwath Road. The junction between Carnwath Road and Wandsworth Bridge Road will be altered at the start of the construction period to enable HGV's to perform a left turn off of Wandsworth Bridge Road onto Carnwath Road.</p> <p>The eastern access will be left turn in right turn out.</p> <p>The western access will be left turn in only.</p> <p>Three sections of parking to be suspended comprising a potential 12 parking spaces on Carnwath Road. Single yellow line parking</p>

Topic	Site-specific requirement
	<p>restrictions will be added where these sections of parking are suspended.</p> <p>An extension to the hours of operation of the existing single yellow line parking restrictions and loading restrictions on Carnwath Road. This will be extended to no parking or loading from 8am to 6pm, Monday to Friday and 8am to 1pm Saturday.</p>
Event restrictions	As per text in <i>CoCP</i> Part A.
River transport	As per text in <i>CoCP</i> Part A.
Other	<p>The diversion of the Thames Path is to be adequately signed.</p> <p>The new route on the eastern boundary is to have high quality directional lighting for security.</p>

6 Noise and vibration

Topic	Site-specific requirement
Control measures	<p>The construction area around the main shaft will be covered by an enclosure/building during the main tunnel construction and secondary lining works. The building will have cladding with a specified sound reduction value. The building openings will be designed to be away from sensitive noise receptors and will be kept closed when not in use at night. Only essential use of openings at night.</p> <p>The western site access will not be routinely used to reduce noise on adjacent properties. See above.</p> <p>Screening or enclose all static plant including pumps.</p> <p>Enclose with suitable structure and acoustic attenuation material concrete batching plant, grout plant, conveyors to load barges and storage / handling areas.</p> <p>Movements of vehicles on the site outside standard hours to be restricted.</p> <p>2.4m hoarding/noise barrier on river wall to screen barge loading areas.</p> <p>The material handling area will be screened by a three sided enclosure and roof clad with suitable noise attenuation material.</p>

Topic	Site-specific requirement
	The barge loading area to be suitably located to consider the noise impacts on riverside properties on both the east and west of the site. See hoarding requirements.
Other	As per text in <i>CoCP</i> Part A.

7 Air quality

Topic	Site-specific requirement
Vehicle and plant emissions	As per text in <i>CoCP</i> Part A.
Dust emissions/control	As per text in <i>CoCP</i> Part A.
Odour	As per text in <i>CoCP</i> Part A.
Other	As per text in <i>CoCP</i> Part A.

8 Water resources

Topic	Site-specific requirement
Control of pollution: surface water / groundwater	All hardstanding (as far as reasonably practicable) on non-foreshore sites to incorporate permeable surfacing.
Control on abstraction	As per text in <i>CoCP</i> Part A.
Ground treatment / dredging	To enable river transport dredging is anticipated.
Other	As per text in <i>CoCP</i> Part A.

9 Land quality

Topic	Site-specific requirement
Site works	As per text in <i>CoCP</i> Part A.
Site-specific issues / mitigation	Due to levels of contaminants that exceed the Probable Effects Level (PEL), dredging will be undertaken using a method to minimise sediment loss and thus mobilisation of contaminants, such as with an enclosed bucket on the backhoe.

10 Waste management and resource use

Topic	Site-specific requirement
Excavated material	As per text in <i>CoCP</i> Part A.
Resource usage	As per text in <i>CoCP</i> Part A.
Other	As per text in <i>CoCP</i> Part A.

11 Ecology (aquatic and terrestrial)

Topic	Site-specific requirement
Protection of habitats	Areas of foreshore used for temporary works will be restored prior to the completion of works, with similar material and to a similar baseline condition. Protection measures for bats apply at this site (no roosts on site).
Protection of trees	Planting of replacement native trees after the construction period required to replace moderate quality trees at site entrance. Ensure protection measures are in place for trees along the eastern boundary of the site.
Other	As per text in <i>CoCP</i> Part A.

12 Historic environment

Topic	Site-specific requirement
Other	As per text in <i>CoCP</i> Part A.

13 Other

Topic	Site-specific requirement
Other	As per text in <i>CoCP</i> Part A.

This page is intentionally blank

Copyright notice

Copyright © Thames Water Utilities Limited January 2013.
All rights reserved.

Any plans, drawings, designs and materials (materials) submitted by Thames Water Utilities Limited (Thames Water) as part of this application for Development Consent to the Planning Inspectorate are protected by copyright. You may only use this material (including making copies of it) in order to (a) inspect those plans, drawings, designs and materials at a more convenient time or place; or (b) to facilitate the exercise of a right to participate in the pre-examination or examination stages of the application which is available under the Planning Act 2008 and related regulations. Use for any other purpose is prohibited and further copies must not be made without the prior written consent of Thames Water.

Thames Water Utilities Limited

Clearwater Court, Vastern Road, Reading RG1 8DB

The Thames Water logo and Thames Tideway Tunnel logo are © Thames Water Utilities Limited. All rights reserved.

DCO-DT-000-ZZZZ-071902

