



Application for Development Consent

Application Reference Number: WWO10001

Examining Authority's Second Written Round of Questions and Requests for Information Response from Thames Water

**Code of Construction Practice Part B: Site Specific Requirements
- Falconbrook Pumping Station (Compare against 23 September 2013)**

Doc Ref: **APP72.9**





Code of Construction Practice Part B: Site-specific requirements

Falconbrook Pumping Station

This page intentionally left blank

Thames Tideway Tunnel

Code of Construction Practice Part B Falconbrook Pumping Station

List of contents

	Page number
1 Falconbrook Pumping Station	1
1.1 Introduction.....	1
2 General Requirements	2
3 Communications and community/stakeholder liaison	2
4 Site operation	32
5 Public access, highway and river transport	3
6 Noise and vibration	4
7 Air quality	5
8 Water resources	5
9 Land quality	5
10 Waste management and resource use	65
11 Ecology (aquatic and terrestrial)	65
12 Historic environment	6
13 Other	6

List of figures

	Page number
Figure 1.1 Falconbrook Pumping Station: Site context and location plan.....	2


This page intentionally left blank

1 Falconbrook Pumping Station

1.1 Introduction

- 1.1.1 All works covered within this document are to be managed and performed to the culture within the Thames Tideway Tunnel vision of 'Zero Incidents, Zero Harm, Zero Compromise'.
- 1.1.2 The *Code of Construction Practice (CoCP)* comprises two parts:
 - a. Part A: General requirements. These measures are applicable project-wide.
 - b. Part B: Site-specific requirements. These are site-specific measures, where there are deviations from the general requirements indicated in Part A.
- 1.1.3 This document comprises the *CoCP* Part B for the Thames Tideway Tunnel project works at Falconbrook Pumping Station site and identifies the detailed site-specific measures including working hours, site set up and servicing arrangements, taking into account the environmental issues and consultations with the London Borough of Wandsworth and other stakeholders.
- 1.1.4 For ease of reference the *CoCP* Part B mirrors the headings in Part A. The *CoCP* Part B sets out site-specific issues and deviations from Part A so where there are no site-specific measures reference should be made to the measures set out in Part A.
- 1.1.1 A plan showing the location of the site is shown in Figure 1.1 below.

Figure 1.1 Falconbrook Pumping Station: Site context and location plan

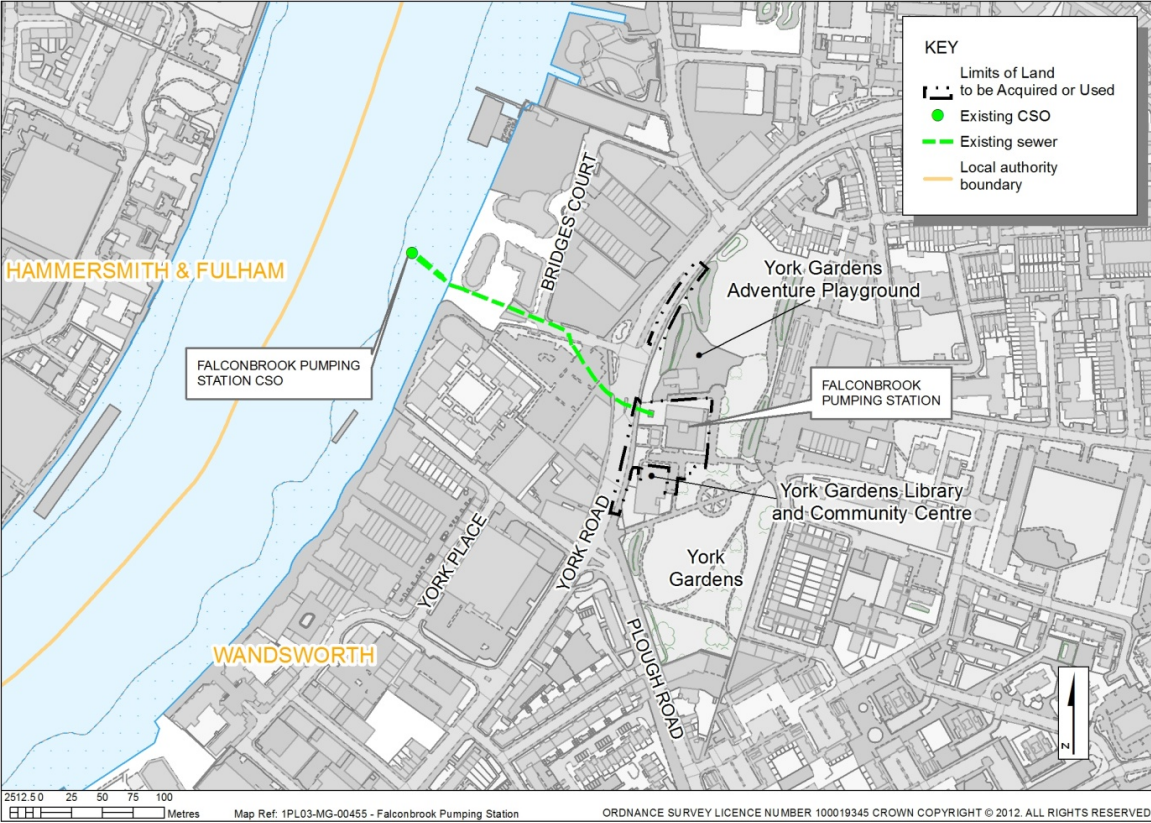

Note: For detailed Limits of Land to be Acquired or Used, refer to drawings in the Book of Plans.

2 General Requirements

2.0.1 As per text in CoCP Part A.

3 Communications and community/stakeholder liaison

3.0.1 As per text in CoCP Part A.

4 Site operation	
Topic	Site-specific requirement
Working hours	<p>This site willshall adhere to the following working hours:</p> <ul style="list-style-type: none"> a. standard b. continuous for duration of the Falconbrook connection tunnel construction. <p>When other types of working hours (<i>CoCP</i> Part A, Table 4.1) are required, these willshall be subject to agreement with the local authority through the Section 61 process.</p>
Site layout	As per text in <i>CoCP</i> Part A.
Site security / hoarding requirements	<p>The hoarding is to be as defined in <i>CoCP</i> Part A para. 4.3.4c, planted hoarding on public facing sections.</p> <p>Increased height of the hoarding adjacent to the York Gardens Library and Community Centre, and along the boundary with the York Gardens Adventure Playground to 3.6m.</p>
River works	As per text in CoCP Part A.
Other items	Site cabin and welfare facilities to be dark green colour to tie in with the planted hoardings.

5 Public access, highway and river transport	
Topic	Site-specific requirement
Site access and gates	<p>New access/egress points are required off York Road.</p> <p>Left turn in from York road and left turn out.</p> <p>The security barrier willshall be positioned to allow a standard rigid tipper vehicle to be wholly off the road whilst awaiting barrier operation.</p> <p>Only emergency access through Lavender Road/housing area is to be permitted unless agreed otherwise.</p> <p>Existing access arrangements for Thames Water operational vehicles willshall be maintained as per the existing regime through Lavender Road.</p>
Traffic management	Access to York Gardens Library and Community Centre, and York Gardens Adventure Playground to

Topic	Site-specific requirement
	<p>be maintained. Existing bus stop on York Road (A3205) willshall be relocated to a suitable alternative position as necessary. The alternative position willshall be located approximately 15m south of the existing location, as agreed with Transport for London.</p> <p>Pedestrian access from York Road to York Gardens willshall be maintained during construction.</p> <p>Disabled parking facility (1 bay) for community centre to be maintained during the construction period at an accessible location.</p> <p>A vehicle marshal or similar willshall be provided where required to ensure the safety of pedestrians crossing the construction access.</p> <p>A small area available for car parking adjacent to the York Gardens Library and Community Centre willshall be suspended during construction.</p> <p>The existing pedestrian access to the York Gardens Library and Community Centre willshall be maintained.</p> <p>Access to the existing pedestrian drop-off area immediately east of the York Gardens Library and Community Centre willshall be maintained.</p>
Event restrictions	N/A
River transport	N/A
Other	The footpath diversion is to shall be adequately signed.

6 Noise and vibration	
Topic	Site-specific requirement
Control measures	<p>As per text in CoCP Part A. <u>Where practicable, alternative methods of non-percussive demolition techniques for the removal and modification of sections of the former pumping station sub-structure would be considered. The proposed methods shall be discussed in advance with LB Wandsworth prior to implementation, in accordance with S61 procedures.</u></p>
Other	The site layout and hoarding design will shall take into account the York Gardens Adventure

Topic	Site-specific requirement
	<p>Playground to the north of the site with regards to noise attenuation and screening.</p> <p>During connection tunnel works outside of standard working hours the use of surface cranes willshall be minimised. This willshall involve the stockpiling of materials/ equipment at the bottom of the shaft for use during the evening and night for removal during standard working hours. In addition the work willshall utilise measures to reduce noise including the use of electric gantry cranes, gas/electric fork lift and measures to reduce noise from skip movements and unloading.</p>

7 Air quality	
Topic	Site-specific requirement
Vehicle and plant emissions	As per text in <i>CoCP</i> Part A.
Dust emissions / control	As per text in <i>CoCP</i> Part A.
Odour	As per text in <i>CoCP</i> Part A.
Other	As per text in <i>CoCP</i> Part A.

8 Water resources	
Topic	Site-specific requirement
Control of pollution: surface water / groundwater	As per text in <i>CoCP</i> Part A.
Control on abstraction	As per text in <i>CoCP</i> Part A.
Ground treatment / dredging	As per text in <i>CoCP</i> Part A.
Other	All hardstanding (as far as reasonably practicable) on non-foreshore sites willshall incorporate permeable surfacing (SuDS/flood risk alleviation).

9 Land quality	
Topic	Site-specific requirement
Site works	As per text in <i>CoCP</i> Part A.
Site-specific issues / mitigation	As per text in <i>CoCP</i> Part A.

10 Waste management and resource use	
Topic	Site-specific requirement
Excavated material	As per text in <i>CoCP</i> Part A.
Resource usage	As per text in <i>CoCP</i> Part A.
Other	As per text in <i>CoCP</i> Part A.

11 Ecology (aquatic and terrestrial)	
Topic	Site-specific requirement
Protection of habitats	As per text in <i>CoCP</i> Part A.
Protection of trees	As per text in <i>CoCP</i> Part A.
Other	As per text in <i>CoCP</i> Part A.

12 Historic environment	
Topic	Site-specific requirement
Other	Granite sets removed from the area adjacent to existing venturi structure and disused public convenience will shall be stored, reinstated/reused.

13 Other	
Topic	Site-specific requirement
Visual	Advance planting within York Gardens as necessary as per agreements with the London Borough of Wandsworth.

Document comparison by Workshare Compare on 07 January 2014 20:50:11

Input:	
Document 1 ID	interwovenSite://VRT-DMS-01/Legal/33752895/1
Description	#33752895v1<Legal> - COCP Falconbrook Sept
Document 2 ID	file://C:\NRPortb\Legal\RKEN\33750244_1.DOCX
Description	33750244_1
Rendering set	no change numbers no summary

Legend:	
<u>Insertion</u>	
Deletion	
Moved from	
<u>Moved to</u>	
Style change	
Format change	
Moved deletion	
Inserted cell	
Deleted cell	
Moved cell	
Split/Merged cell	
Padding cell	

Statistics:	
	Count
Insertions	26
Deletions	26
Moved from	0
Moved to	0
Style change	0
Format changed	0
Total changes	52

Copyright notice

Copyright © Thames Water Utilities Limited January 2014.
All rights reserved.

Any plans, drawings, designs and materials (materials) submitted by Thames Water Utilities Limited (Thames Water) as part of this application for Development Consent to the Planning Inspectorate are protected by copyright. You may only use this material (including making copies of it) in order to (a) inspect those plans, drawings, designs and materials at a more convenient time or place; or (b) to facilitate the exercise of a right to participate in the pre-examination or examination stages of the application which is available under the Planning Act 2008 and related regulations. Use for any other purpose is prohibited and further copies must not be made without the prior written consent of Thames Water.

Thames Water Utilities Limited

Clearwater Court, Vastern Road, Reading RG1 8DB

The Thames Water logo and Thames Tideway Tunnel logo are © Thames Water Utilities Limited. All rights reserved.

